



Georgetown Independent School District 2018 Bond Program

7 July 2020

Project: Wolf Ranch Elementary School

Project Info

A/E Firm: Huckabee
Contractor: Bartlett Cocke General Contractors
Project Delivery Method: Construction Manager-at-Risk
Financial Status:
 Guaranteed Max Price: \$29,668,098.00
 Paid to Date: \$26,593,350.00
 Balance: \$3,074,748.00

Scope of Work

New Elementary School (PK - 5th grade)
 - 17.669 acres
 - 122,802 SF (2 stories)
 - Geothermal HVAC System
 - SolaTubes in Gym
 - 251 Parking Spots

Current Status


Asphalt Paving: Complete
 Interior Finishes: Finalizing
 Kitchen Eq: Complete
 Final Inspections: Being scheduled with City Inspectors

Substantial Completion: ECD 20 Jul
 Furniture Delivery Schedule: EDD 27 Jul

Project Schedule

A/E Start Design: February 26, 2018
 GMP Proposal Date: April 10, 2019
 Notice to Proceed: May 20, 2019
 Construction Start: May 21, 2019
 Substantial Complete:
 Complete

Photos

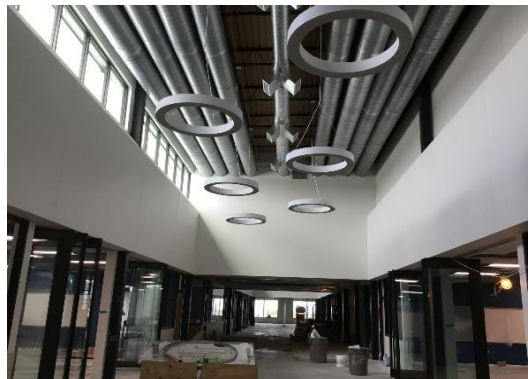

Mobilize

Substantial Completion Closeout
