



Georgetown Independent School District

LEAD GROW SERVE

2015 Bond Program

Dr. Fred Brent, Superintendent of Schools

603 Lakeway Dr.

Georgetown, Texas 78628


April 1, 2016

Project Info: GHS Renov. (Package B)

Facilities & Construction: David Biesheuvel - Exec Dir.

GISD Project Manager	Mario Alaniz
Contact Information	512/943-5129
Project Delivery Method	CM@R
A/E Firm:	Huckabee Architects
Contractor:	Bartlett Cocke
Construction Budget:	\$14,973,509.00
Expenses paid to date:	\$0.00
Balance:	\$14,973,509.00

Photos

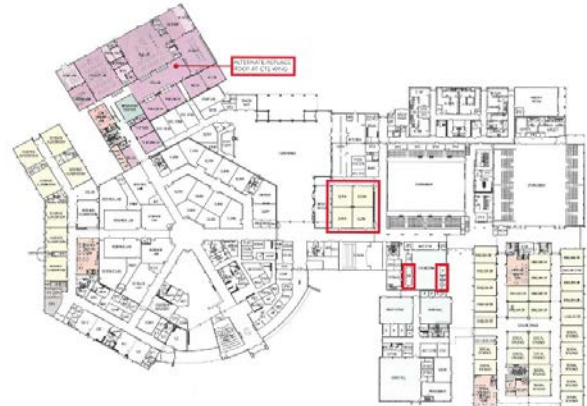

Scope of Work

The south academic wing, fine arts wing, north wing science labs and the vocational wing will be renovated.

Current Status

Project has 3 Phases of Work:
 Phase 1 - 12/19/16 - 8/10/17
 Phase 2 - 5/30/17 - 12/20/17
 Phase 3 - 5/31/17 - 8/14/2018
 All interior walls and ceilings in the south wing have been demoed. Rework of existing underfloor plumbing is nearing completion. Metal stud framing for new interior walls has begun.



Project Schedule

A/E Start:	October 1, 2016
Bid Date:	December 12, 2016
Construction Start:	February 10, 2017
Substantial Complete: Ph 1	August 10, 2017
Complete	August 14, 2018

