



Georgetown Independent School District

LEAD GROW SERVE

2015 Bond Program

Dr. Fred Brent, Superintendent of Schools

603 Lakeway Dr.

Georgetown, Texas 78628

August 1, 2017

Project Info: New Purl ES

Facilities & Construction: David Biesheuvel - Exec Dir

GISD Project Manager: Mario Alaniz

Contact Information: 512/943-5129

Project Delivery Method: CSP

A/E Firm: Huckabee Architects

Contractor: Joeris General Contractors

Financial Status:

Construction Budget: \$24,900,000.00

Expenses paid to date: \$19,997,727.00


Balance: \$4,902,273.00

Photos




Scope of Work

A new 115,616 sf elementary school. All existing buildings will be demolished.

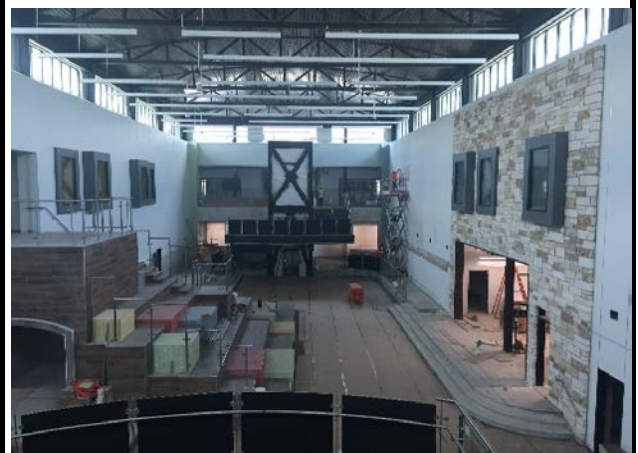

Current Status

Purl ES is nearing completion. Areas 1, 2, 4 & 5 have a TCO from the City of Georgetown for furniture installation. All parking areas and drives are complete. Landscaping is in progress. Grand opening is scheduled for August 14, 2017. Entire facility is scheduled for use by August 17, 2017. Punchlist items will be done during school hours and after hours.

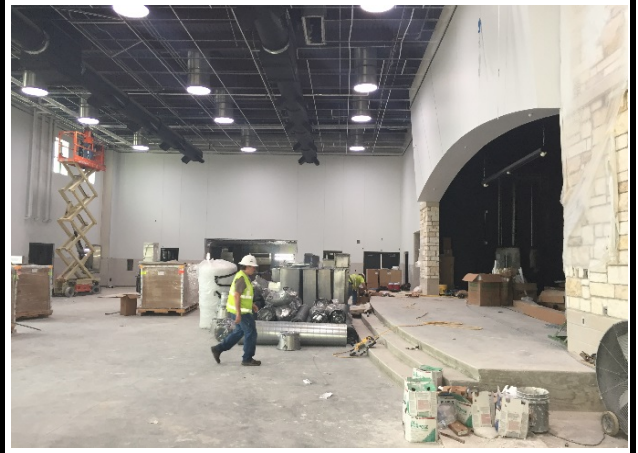

Project Schedule

A/E Start: November 15, 2015

Bid Date: May 24, 2016

Construction Start: July 20, 2016

Substantial Complete: August 17, 2017

Complete: Sept/15/2017

