



Georgetown Independent School District

LEAD GROW SERVE

2015 Bond Program

Dr. Fred Brent, Superintendent of Schools

603 Lakeway Dr.

Georgetown, Texas 78628


December 1, 2016

Project Info: GHS Renov. (Package B)

Facilities & Construction: David Biesheuvel - Exec Dir.

GISD Project Manager	Mario Alaniz
Contact Information	512/943-5129
Project Delivery Method	CM@R
A/E Firm:	Huckabee Architects
Contractor:	Bartlett Cocke
Construction Budget:	\$16,250,000.00
Expenses paid to date:	\$0.00
Balance:	\$16,250,000.00

Photos

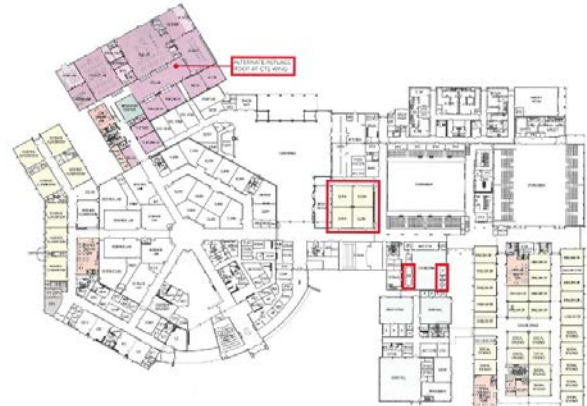

Scope of Work

The south academic wing, fine arts wing, north wing science labs and the vocational wing will be renovated.

Current Status

Huckabee Architects has completed construction documents. It is anticipated to recommend a GMP to the Board of Trustees in January, 2017. A pre-bid conference was held on November 29, 2016.



Project Schedule

A/E Start:	July 6, 2016
Bid Date:	December 13, 2016
Construction Start:	February 1, 2017
Substantial Complete:	August 14, 2018
Complete:	August 24, 2018

