



Georgetown Independent School District

LEAD GROW SERVE

2015 Bond Program

Dr. Fred Brent, Superintendent of Schools

603 Lakeway Dr.

Georgetown, Texas 78628


July 1, 2016

Proj Info: GHS/EVHS HVAC Upgrades

Photos

Facilities & Construction: David Biesheuvel - Exec Dir.

GISD Project Manager	Mario Alaniz
Contact Information	512/943-5129
Project Delivery Method	JOC
A/E Firm:	Estes McClure Associates
Contractor:	Braun & Butler
Construction Budget:	\$1,097,937.00
	\$0.00
Expenses paid to date:	\$79,475.42
Balance:	\$1,018,461.58

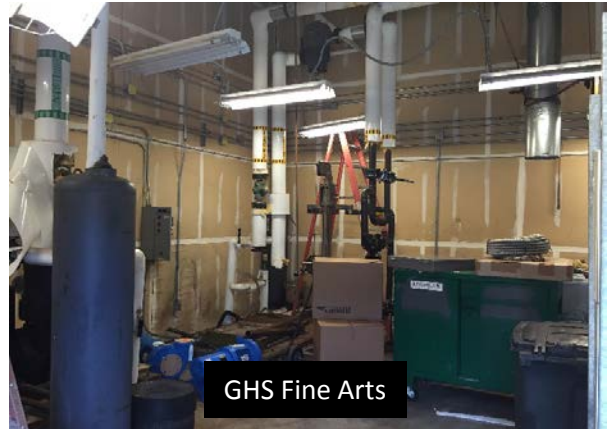

GHS Fine Arts

Scope of Work

Replace chillers/boilers/HVAC at GHS Fine Arts and PAC
 HVAC upgrades to EVHS Weight Room



GHS Fine Arts

Current Status

EMA has completed the construction documents. A GMP has been received and will be presented to the Board of Trustees at the April 11, 2016 meeting. A pre-construction meeting was held on April 19, 2016. Contractor has begun work. **Contractor has completed the work at the EVHS athletic building. Work at the GHS Fine Arts and PAC is on-going. Boiler and Chiller have been installed at the Fine Arts area.**



HVAC Upgrades - EVHS

Project Schedule

A/E Start:	January 25, 2016
Proposal Date:	March 30, 2016
Construction Start:	May 13, 2016
Substantial Complete:	July 29, 2016
Complete	August 15, 2016

