



Georgetown Independent School District

LEAD GROW SERVE

2015 Bond Program

Dr. Fred Brent, Superintendent of Schools

603 Lakeway Dr.

Georgetown, Texas 78628

July 1, 2016

Project Info: Stadium Turf Replacem't

Facilities & Construction: David Biesheuvel - Exec Dir.

GISD Project Manager	Mario Alaniz
Contact Information	512/943-5129
Project Delivery Method	CSP - BuyBd
A/E Firm:	Sports Design Group
Contractor:	Hellas Construction, Inc.
Construction Budget:	\$957,500.00
	\$0.00
Expenses paid to date:	\$880,463.01
Balance:	\$77,036.99

Photos




GHS Practice Field

Scope of Work

Replace turf at the GISD Athletic Complex and the Georgetown HS Practice Field.

Current Status

GISD received bid proposals on January 26, 2016. A recommendation to award was made to the Board of Trustees on February 16, 2016. Construction anticipated to start on April/June 2016. A Pre-construction meeting was held on Monday, April 11, 2016 at 1:00 pm. **Contractor has completed the installation of the new turf on the GHS practice field. Contractor has moved all its work forces to the GISD Stadium field turf replacement. Anticipated completion date of all work is the week of July 18, 2016.**

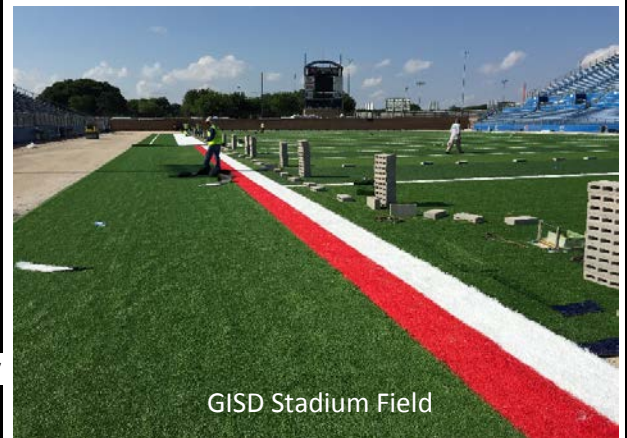

GISD Stadium Field

Project Schedule

A/E Start:	November 15, 2015
Bid Date:	January 26, 2016
Construction Start:	April 18, 2016
Substantial Complete:	July 11, 2016
Complete	August 1, 2016



GISD Stadium Field

