



# Bond Update

20 August 2018






# 2015 Bond Projects

- Tippit MS Renovations/Additions
- Renovate Williams Campus
- West Side Transportation Terminal
  
- Renovate Georgetown HS - COMPLETED
- Construct Secure Entries - Multi Facilities - COMPLETED
- Rehab Pavement - GHS South Parking & Support Services - COMPLETED

# Tippit MS Renovations/Additions



- City issued Temp C.O. - 8/10/18
- All areas open for use except:
  - Art rooms (using portable)
  - 2<sup>nd</sup> floor flex rooms above art
  - Cafeteria/Kitchen and drama classroom
- Complete all areas - Oct 2018
  - Demo old Cafe/Kitchen (Dec 2018)

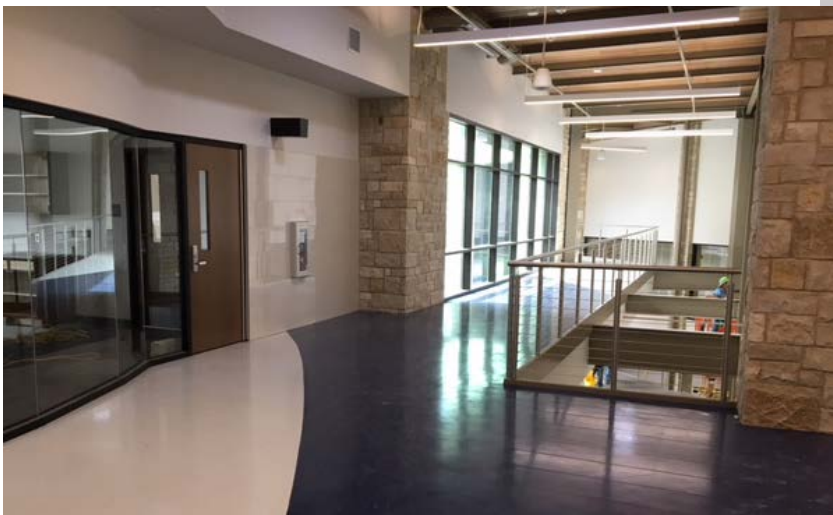

# Renovate Williams Campus

- Landscaping - 90% complete
- Floor Tile - started installation 8/13
- Polish concrete floors - in progress
- Install door/window frames - in progress



# West Side Transportation Terminal



- Complete
  - Buses started operating out of facility on 8/20
- Temporary yard lights and power in use

