Georgetown Independent School District
2018 Bond Program
1 October 2019

Project: EVHS Wrestling Room Addition

Project Info

A/E Firm: Huckabee
Contractor: Braun & Butler Construction
Project Delivery Method: Construction Manager-at-Risk
Financial Status:

Guaranteed Max Price:	$795,336.00
Paid to Date:	$0.00
Balance:	$795,336.00

Scope of Work

Addition to EVHS Field House for Wrestling Room
- 2,475 SF

Current Status

Bldg pad - complete
Grade Beams in progress
Pour concrete slab - mid-Oct

Scheduled Completion: 2/29/20

Project Schedule

A/E Start Design:	February 26, 2018
GMP Proposal Date:	July 22, 2019
Notice to Proceed:	September 3, 2019
Construction Start:	September 3, 2019
Substantial Complete:	
Complete	

Photos

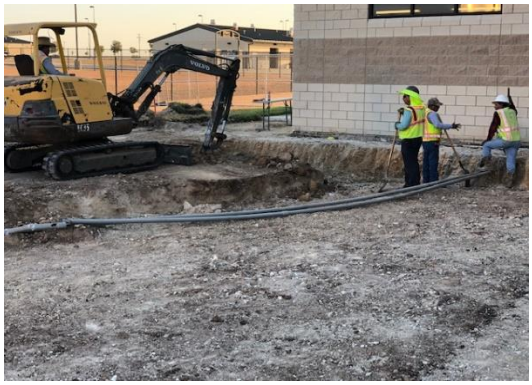

Mobilize — Substantial Completion — Closeout
